



PROJECT: Piney Cr. Stabilization (Tower to Liverpool)

DESCRIPTION: Design and construction of stream stabilization of Piney Creek. UDFCD joint project.

BUDGET: \$550,000

STATUS: Construction underway

CHANGE SINCE LAST REPORT:
CONSTRUCTION 70% COMPLETE

MILESTONES

Construction Completion: April 2011



PROJECT NAME: PINEY CREEK (TOWER TO LIVERPOOL)



PROJECT NAME: PINEY CREEK (TOWER TO LIVERPOOL)



PROJECT: West Toll Gate Creek at Foxhill Park

DESCRIPTION: Design and construction of stream stabilization improvements


BUDGET: \$350,000

STATUS: CONSTRUCTION UNDERWAY

CHANGE SINCE LAST REPORT: CONSTRUCTION 50% COMPLETE

MILESTONES

Construction Completion: April 2011

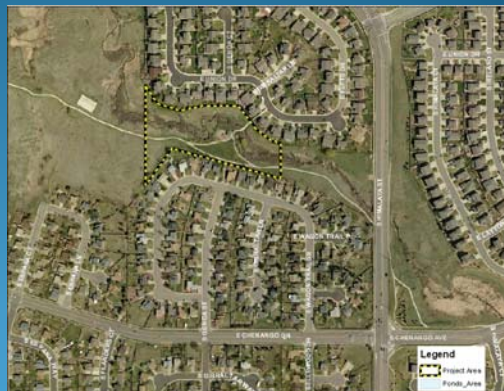

PROJECT NAME: WEST TOLLGATE



PROJECT NAME: WEST TOLLGATE



PROJECT: Lone Tree Creek Pond L-1 West

DESCRIPTION: Design and construction of the regional stormwater pond.

BUDGET: \$225,000

STATUS: Final design complete; Section 404 Permit acquired.

CHANGE SINCE LAST REPORT:
Contract Awarded March 4, 2011

MILESTONES:

Construction Start: April 4, 2011



ACTIVE DESIGN PROJECTS (FALL 2011 CONSTRUCTION START)

<u>PROJECT</u>	<u>TOTAL ESTIMATED COST (\$)</u>	<u>SEMSWA ESTIMATED COST (\$)</u>
CHERRY CREEK STABILIZATION @ ECO PARK	3,100,000	1,382,000
LINCOLN EXECUTIVE CENTER EAST POND	325,000	325,000
WINDMILL CREEK POND W-1 (PHASE 1)	110,000	110,000
FOREST PARK - TRIBUTARY B STABILIZATION	220,000	220,000
LONE TREE CREEK POND L-2 (PHASE 1)	295,000	295,000
GOLDSMITH GULCH (PHASE 1) - CALEY CULVERT	265,000	220,000
LITTLE DRY CREEK REACH 6 STABILIZATION	650,000	650,000
TOTAL	3,750,000	2,032,000
